

Job Costing Report

Dart Aerospace Ltd.
Hawkesbury

Nov 08, 2005
10:39 am

Work Order No : 0023841
Project Name : pB67-43001-243
Project For : WK531
Work Order Type : Main
Main WO Number :
House Part Number : pB67-43001-243
Description : Handle Arm Extension
Manufactured : Yes
Amount Req'd : 1
Amount Done : 0
Start Date : 07-19-05
Est Finish Date :
Act Finish Date :
Drawings Req'd : No
Ok for Approval :
Approval Rec'd :

Department Code:
Burden Flags : NNNNNNNN
WO Status : Open
Invoice State : Not Invoiced
Invoice Date :
Invoice Number :
Invoice Amount : 0.00
Order Entry No :
OE Value : 0.00
Est Margin : 0.000%
Actual Margin : 0.000%
\$0 Posted to Finished Goods

	Estimated	Actual	Var. %	Posted	To Post
Material Cost :	0.00	0.00	0.00	0.00	0.00
Engineering Hours :	0.00	0.00	0.00		
Engineering Cost :	0.00	0.00	0.00	0.00	0.00
Production Hours :	0.00	0.00	0.00		
Production Cost :	0.00	0.00	0.00	0.00	0.00
Packaging Hours :	0.00	0.00	0.00		
Packaging Cost :	0.00	0.00	0.00	0.00	0.00
OverHead Hours :	0.00	0.00	0.00		
OverHead Cost :	0.00	0.00	0.00	0.00	0.00
CNC Hours :	0.00	0.00	0.00		
CNC :	0.00	0.00	0.00	0.00	0.00
Misc. Hours :	0.00	0.00	0.00		
Misc. :	0.00	0.00	0.00	0.00	0.00
Burden :	0.00	0.00	0.00		
Total Cost :	0.00	0.00	0.00		
Margin :	0.000	0.000			
Selling Cost :	0.00	0.00			

	Estimated	Actual
Labour Hrs/Amount Done :	0.00	0.00
Profits/(Loss) :	0.00	0.00

DART AEROSPACE LTD

Work Order:

23349

Description:

Kurdle Oval Extension

Part Number:

B67-43001-~~187-243~~

Dwg:


B67-43001 Rev B p 21


Qty:


1


Page 1 of 1

Step	Location	Procedure Issue Traveller	By	Date	Qty
1	DC				
2	ML	Turn on per Rev B67-43001 Material: 100" x 1.187" wall (meets 1.00 x 1.187) Batch 18101	JM	05.07.11	1
3	DC	Inspect Park as they come off the machine	E	05.07.10	1
4	ML	Reburn	E	05.07.10	1
5	MM	Fill as per Rev B67-43001	E	05.07.10	1
6	DC	Inspect Park as they come off the machine	E	05.07.10	1
7	DC	Second Chk.	JM	05.07.10	1
8	MM	Reburn	E	05.07.10	1
9	AST	Identify Stack	D	05/07/11	1
10	AC	Coat/Paint 29.95 SAC 05/08/09 Level 21	D	05/08/09	1
Rev	Date	Change	Revised By	Approved	
		New Issue			

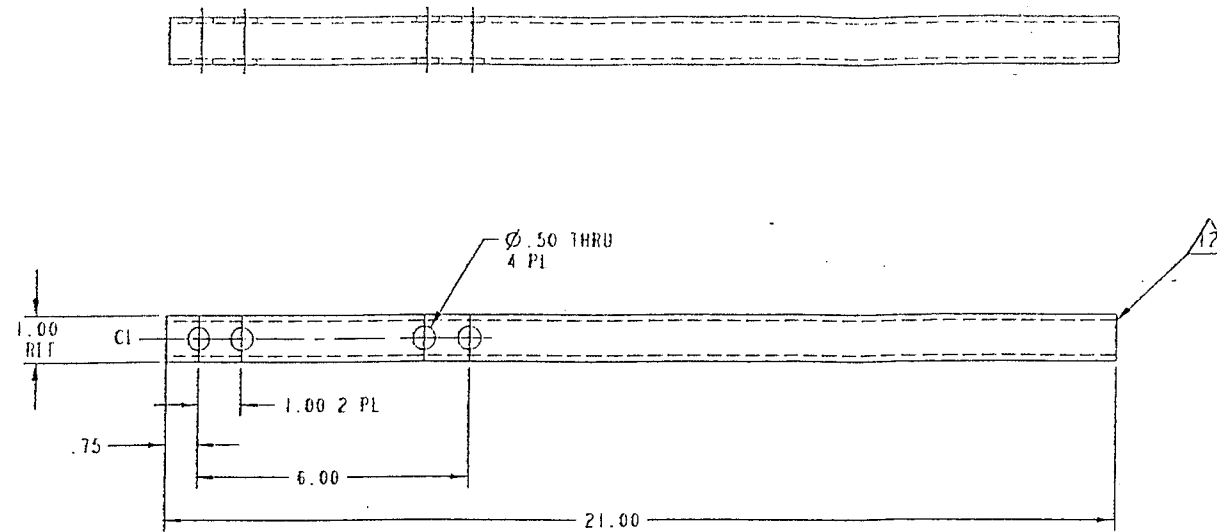



① -239 SQUARE TUBE 
 MATL: 1.00 SQ X .125 WALL, 6061-T6
 QQ-A-200/8
 SCALE 0.500

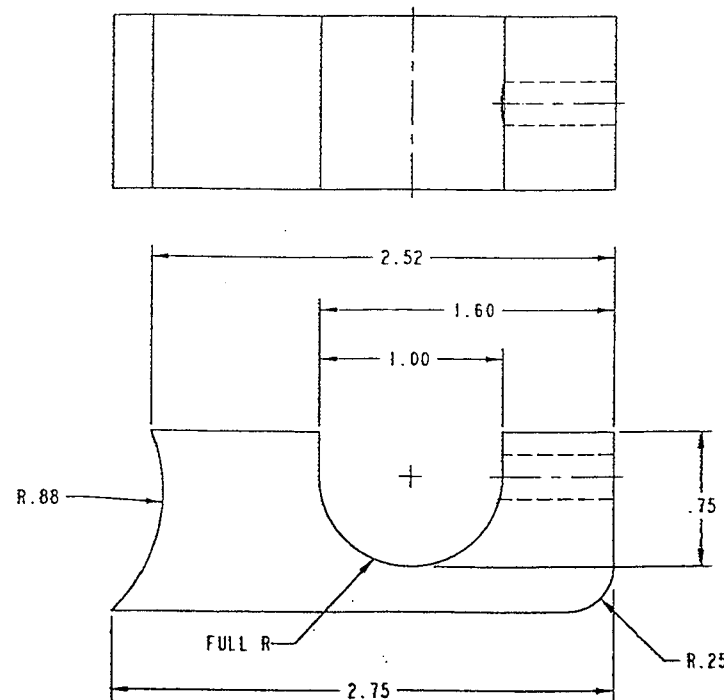



-241 TUBE DETENT CLIP 
 MATL: 1.00 SQ, 6061-T6
 QQ-A-200/8
 SCALE 2.000

REPLACED BY
 ① XM D3440-9

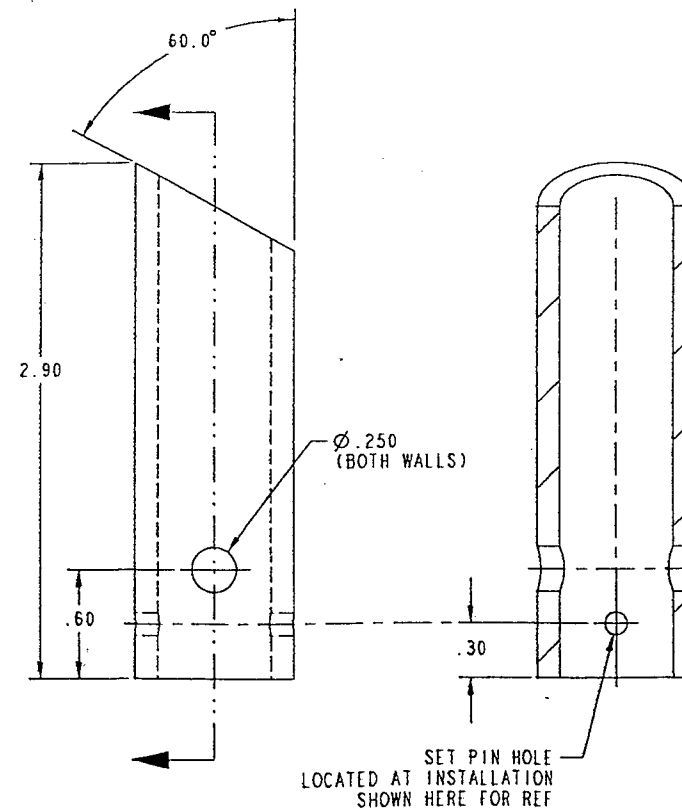

① -243 TUBE HANDLE EXTENSION 
 MATL: .875 OD X .125 WALL, 6061-T6
 QQ-A-200/8
 SCALE 2.000

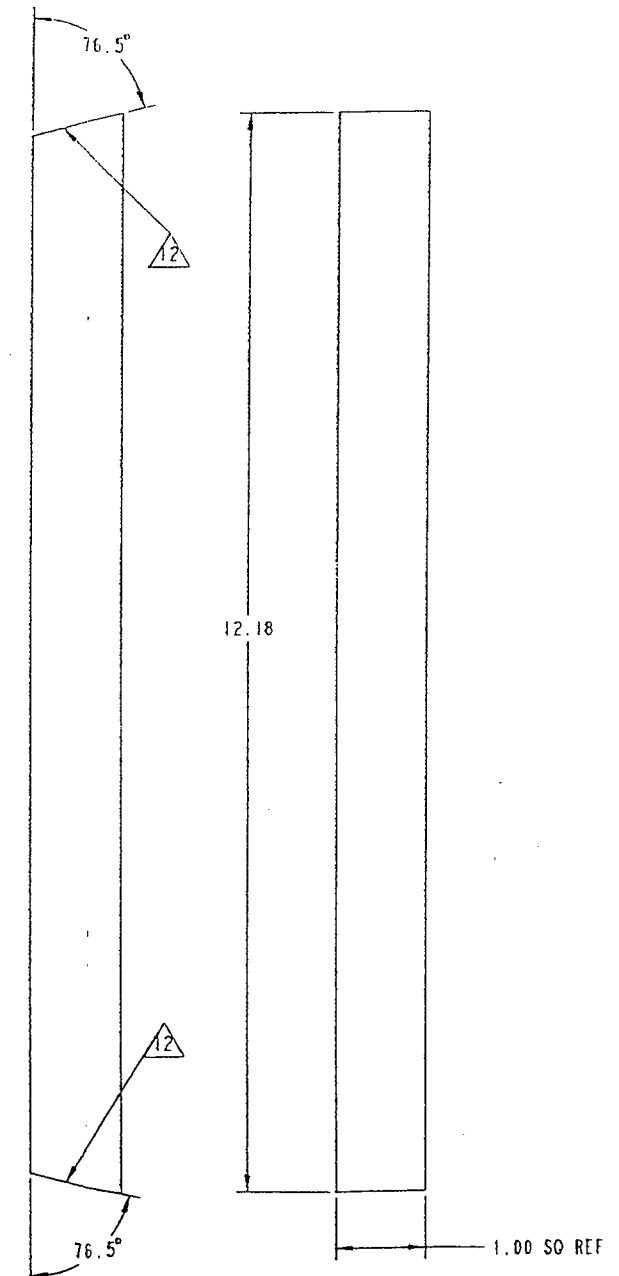

① -139 SQUARE TUBE 
 MATL: 1.00 SQ X .125 WALL, 6061-T6
 QQ-A-200/8
 SCALE 1.000

REFERENCE ONLY

PREMIER AVIATION, INC.			
2521 Aviation Parkway, Grand Prairie, Texas 75052			
SIZE	CODE IDENT NO.	DWG NO.	REV.
D	OSUV8	B67-43001	B
SCALE:	W1:	SHEET	21 of 45

ORIGINAL
